


Current Project Construction Area (shown by the areas the the thick red border) for the month of November will be the continued testing of the new mains from Benedict Ave. and north, the completion of the interconnection on Crest St. and the possibly the extension of the main on Benedict Ave. to Wayne St. Transfer of existing services to the new main is also planned.

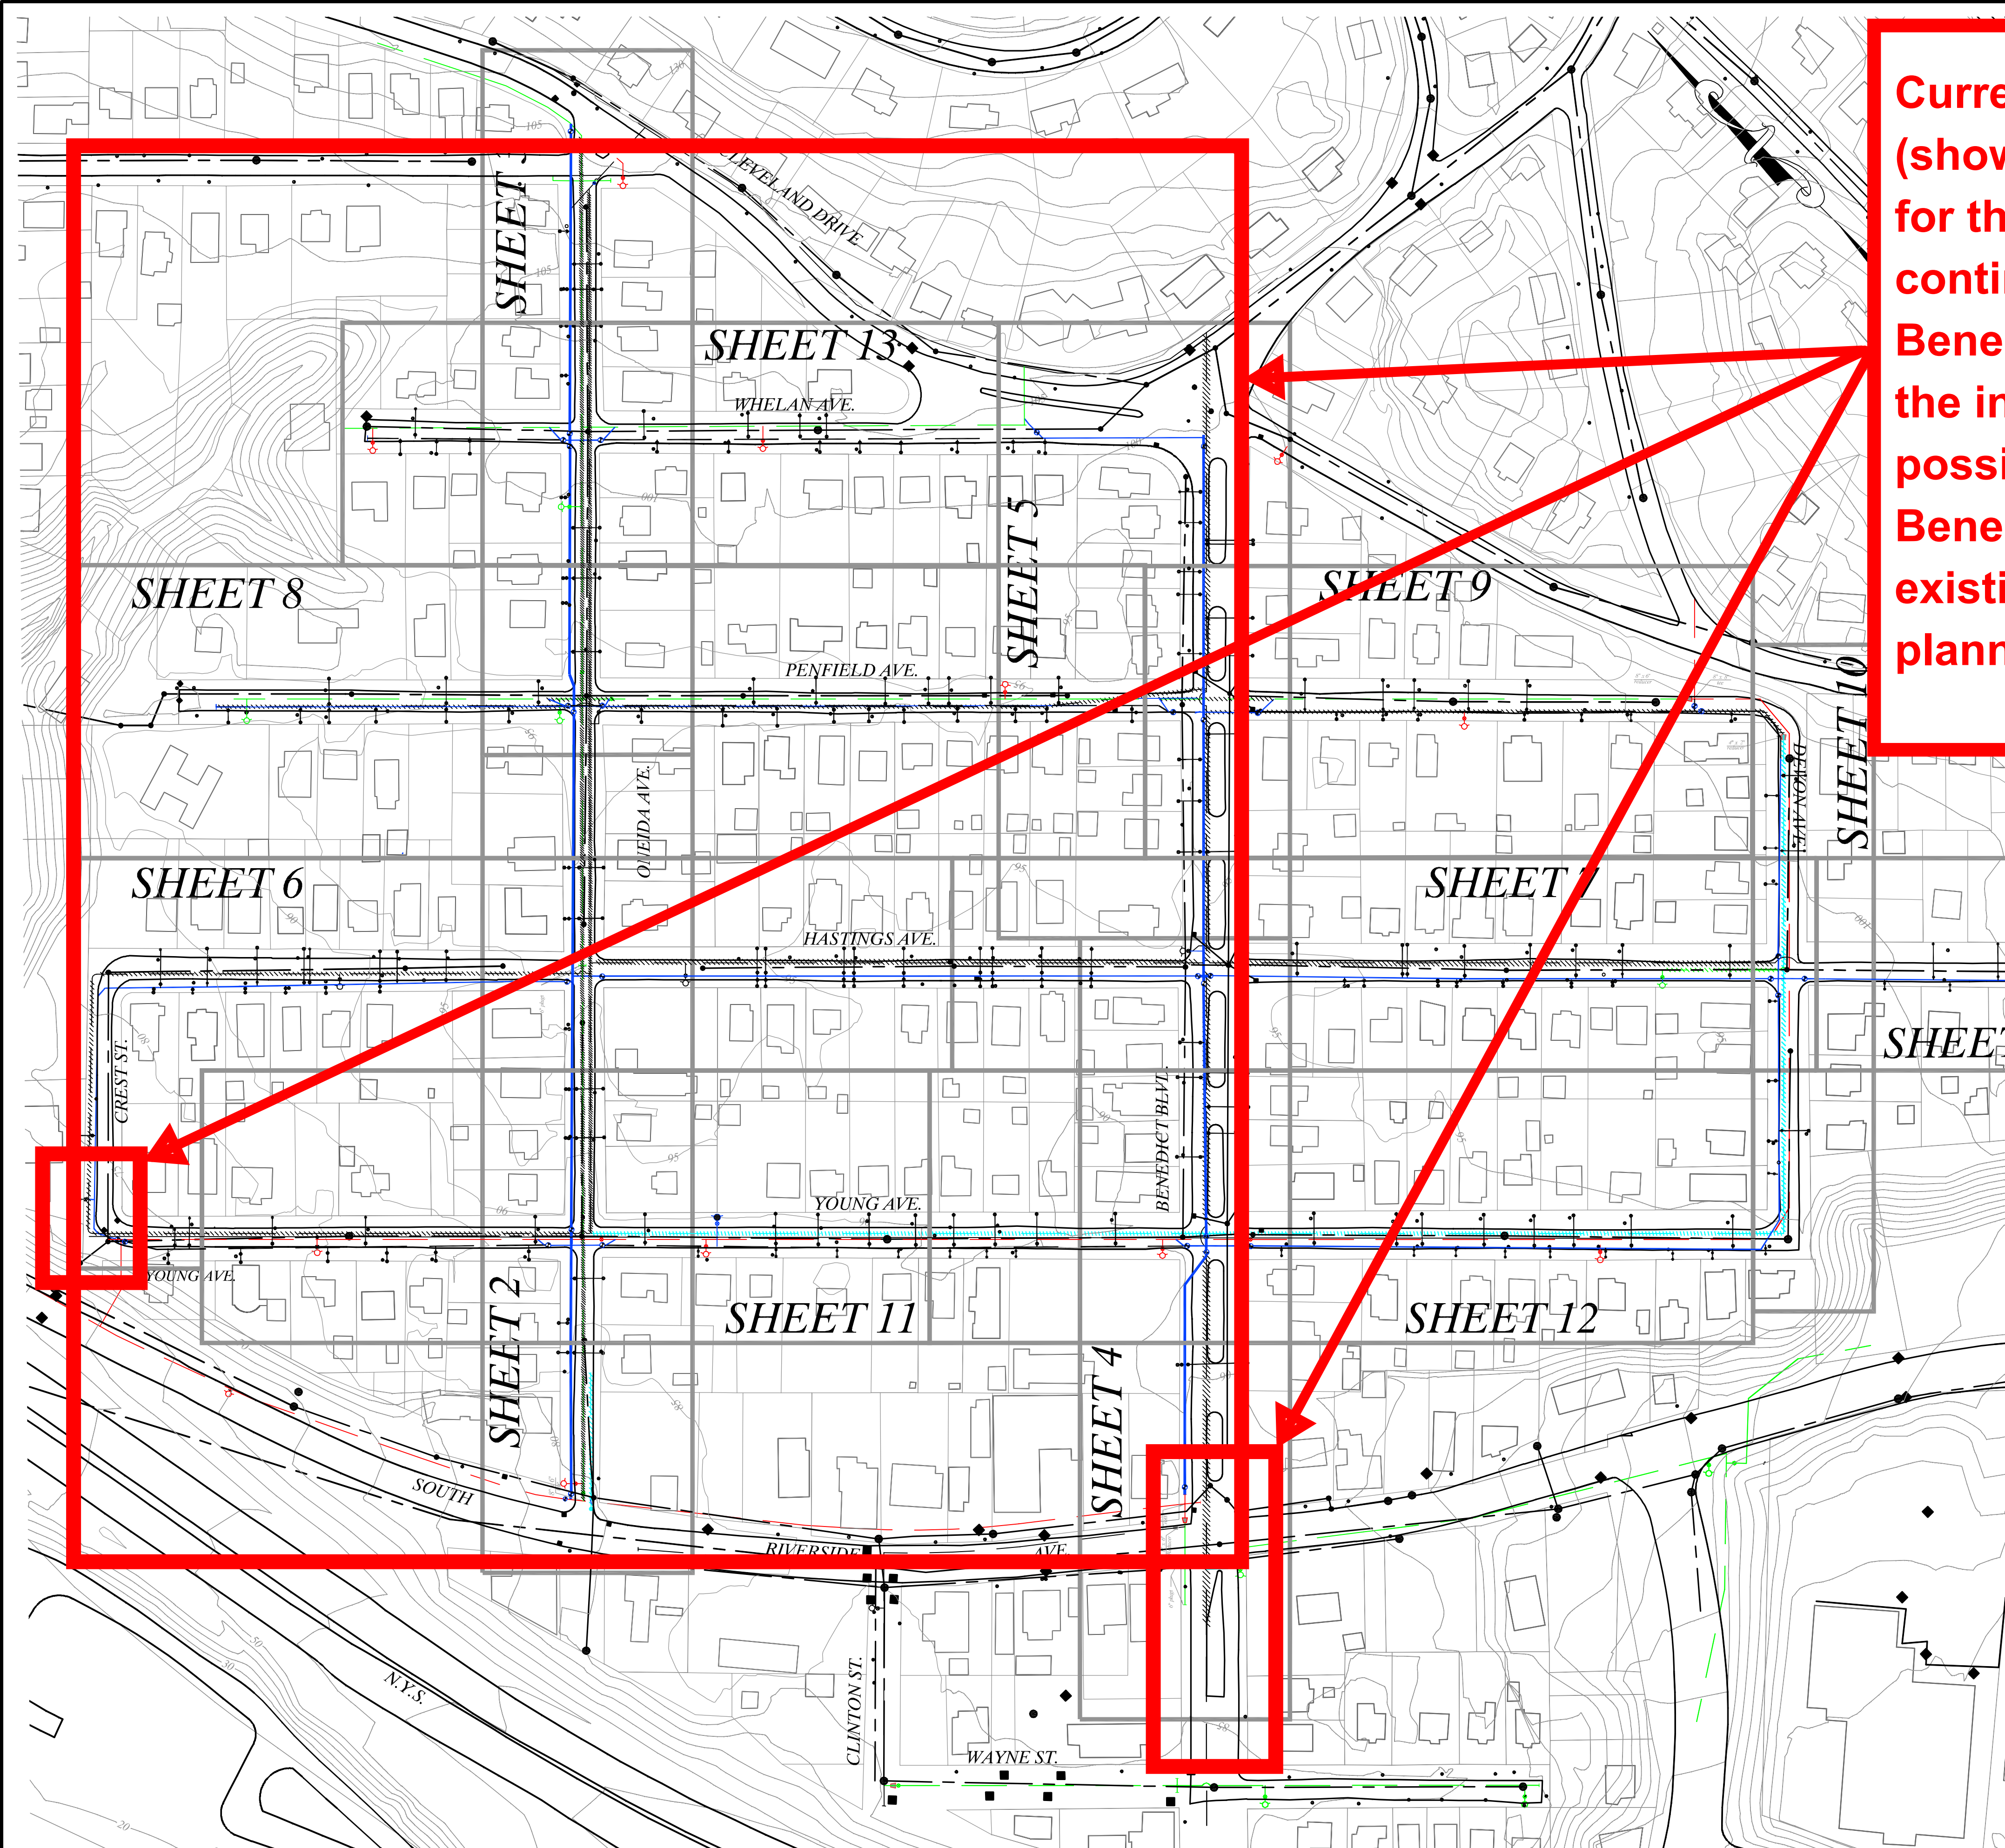

NOTES:

1. EXISTING TOPOGRAPHIC MAPPING FROM VILLAGE OF CROTON ON HUDSON GIS SURVEY.
2. EXISTING UTILITIES FROM VILLAGE OF CROTON ON HUDSON GIS SURVEY.
3. CONTRACTOR TO NOTIFY ALL UTILITY COMPANIES PRIOR TO START OF WORK TO FIELD LOCATE EXISTING UTILITIES.
4. PRIOR TO ANY CONSTRUCTION RELATED ACTIVITIES, THE CONTRACTOR SHALL COMPLY WITH INDUSTRIAL CODE RULE 53, TELEPHONE # 800-245-2828.
5. ALL PROPOSED WATER MAINS SHALL BE CEMENT LINED DUCTILE IRON PIPE, PRESSURE CLASS 54.
6. PROPOSED WATER SERVICE LOCATIONS ARE FOR ESTIMATING PURPOSES ONLY.
7. UNLESS OTHERWISE NOTED, ALL WATER SERVICES ARE TO BE 3/4" COPPER.

PROPOSED WATER MAIN REPAIRS AND IMPROVEMENTS TO THE VILLAGE OF CROTON ON HUDSON WATER DISTRIBUTION SYSTEM

VILLAGE OF CROTON ON HUDSON WESTCHESTER CO., N.Y.

Kellard Engineering & Consulting, P.C.
CIVIL ENGINEERS • SITE & ENVIRONMENTAL PLANNERS

500 Main Street • Armonk, N.Y. 10504
(914) 273-2323

5	APRIL 6, 2005	HEALTH DEPT. COMMENTS
4	JANUARY 31, 2005	HEALTH DEPT. APPLICATION
3	DECEMBER 15, 2004	VILLAGE COMMENTS
2	APRIL 5, 2004	W.C.H.D. COMMENTS
1	MARCH 1, 2004	
date:	MARCH 1, 2004	sheet: 1
project no:	CRT 600	

UNAUTHORIZED ADDITIONS, MODIFICATIONS AND/OR ALTERNATIONS TO THESE PLANS IS A VIOLATION SECTION 7209(2) OF THE NEW YORK STATE EDUCATION LAW.

